Shinmura Bridge Construction Update

Sep 2026 Vol.3

September brought frequent rain to Japan, and Kamikochi was no exception, with rainfall recorded on 23 days. Despite the weather, the area remained busy with hikers, and visitor numbers are expected to increase as the autumn foliage season begins. Safety remains our top priority.On site, concrete work for the anchor blocks and steel tower foundations is progressing steadily. We are making a final push toward tower assembly in late October!


On-Site Construction Progress

The photo on the right shows an anchor block. The angled steel anchor frame holds wires at its tip to support the tower. With loads of up to 240 tonnes acting here, precise construction and concrete quality are critical. As concrete delivery takes nearly 80 minutes, each pour is a long operation.



The photo below shows our company-owned tower materials, recently trucked in from Tsu City, Mie Prefecture. Painted dark brown to suit Kamikochi's scenery, they blend beautifully with nature. Standing up to 28 m tall, the tower will be a highly visible symbol of this project!



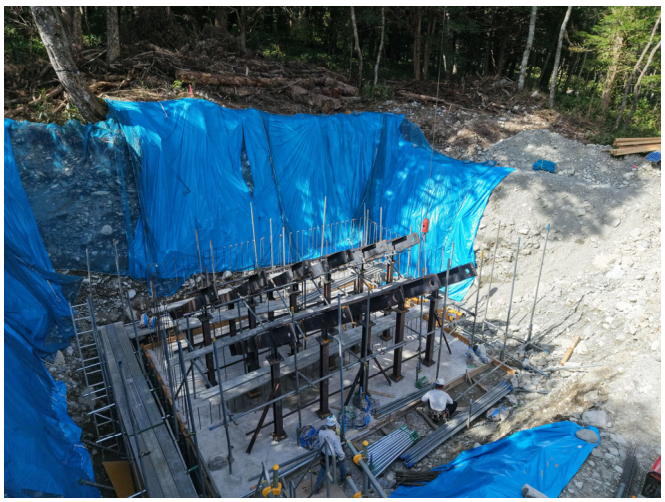

Key Schedule for October

[Concrete Pouring Schedule]
Thu, Oct 1
Tue, Oct 6
Wed,Oct 7
Fri, Oct 9
Tue, Oct 20

[Other]
Tower assembly: from Wed, Oct 21

*Schedule is subject to change depending on weather and work progress.

【Comments and Inquiries Regarding Construction】

JFE・Yamaura Special Construction Joint Venture

3094-2 Hata, Matsumoto City, Nagano Prefecture 390-1401
Tel: 0263-31-5238

Site Representative: Kurita
